

ABN 31 105 704 078

13 Brock Street, Thomastown

Victoria 3074

(P) +61 3 9464 4617



LEVEL 1 INSPECTION & TESTING LUCAS ESTATE - STAGE K1

Prepared for Bild Group

Report Reference: GS6240.1 AA

Date: 27 July 2022

ABN 31 105 704 078

13 Brock Street, Thomastown

Victoria 3074

(P) +61 3 9464 4617



PROJECT DETAILS

Project Reference	GS6240.1	Rev	AA
Project Title	Lucas Estate Stage K1		
Project Location	Lucas	State	VIC
Date	27 July 2022		

CLIENT DETAILS

Prepared For (Client)	Bild Group
Client Address	133 Metrolink Circuit, Campbellfield VIC 3061

DISTRIBUTION

Original Held By	Ground Science Pty Ltd
One (1) Electronic Copy	Bild Group

This document presents the results of the Level 1 Inspection and Testing performed by Ground Science for the aforementioned project, as the nominated project Geotechnical Inspection & Testing Authority (GITA). This report is detailed for the sole use of the intended recipient(s). Should you have any questions related to this report please do not hesitate to contact the undersigned.

AUTHOR:



Anton Manoj
Geotechnical Engineer

REVIEWED:



Gee Singh, RPEng
Senior Geotechnical Engineer

Table of Contents

- 1. INTRODUCTION 1
- 2. SCOPE OF WORK 1
 - 2.1 AREAS OF WORK 1
 - 2.2 PLACEMENT METHODOLOGY 1
- 3. INSPECTION AND TESTING 2
 - 3.1 SUBGRADE PREPARATION 2
 - 3.2 CONSTRUCTION MATERIALS 2
 - 3.3 FILL CONSTRUCTION 2
 - 3.4 RESULTS OF COMPACTION CONTROL TESTING 3
 - 3.5 FINAL SURFACE LEVELS 3
- 4. COMPLIANCE 3
- 5. UNDERSTANDING LEVEL 1 INSPECTION & TESTING 4
- 6. LIMITATIONS 5
- 7. REFERENCES 6

APPENDICES

- APPENDIX A FIELD DENSITY TEST SUMMARY SHEETS AND TEST LOCATIONS
- APPENDIX B FIELD DENSITY TEST REPORT SHEETS
- APPENDIX C SITE PHOTOGRAPHS

1. INTRODUCTION

This report presents the results of the inspection activities, compaction control and laboratory testing services performed by Ground Science Pty Ltd for the development at Lucas Estate Stage K1, Lucas, Victoria (the site).

Level 1 Inspection & Testing, as defined in AS3798 (2007) 'Guidelines on Earthworks for Commercial and Residential Developments' provides for full-time inspection of the construction of controlled fill and compaction testing in accordance with AS1289 'Methods of Testing Soils for Engineering Purposes'. The primary objective of Level 1 Inspection & Testing, according to AS3798 (2007), is for the geotechnical inspection and testing authority (GITA) to be able to express an opinion on the compliance of the work.

Ground Science performed the role of the project GITA. The testing services described in this report were undertaken by an experienced GITA site representative.

2. SCOPE OF WORK

2.1 AREAS OF WORK

The areas requiring Level 1 Inspection & Testing are shown in **Appendix A**, which is based on plans prepared by Integra (LUK1-CD-701 REV 1). This report details the Level 1 earthworks process performed onsite which commenced on 10 March 2022 and was completed on 2 June 2022, including 2 full days of filling operations.

2.2 PLACEMENT METHODOLOGY

The placement of controlled fill on the above-mentioned areas was carried out in accordance with Level 1 fill procedures as detailed in AS3798 (2007) 'Guidelines on Earthworks for Commercial and Residential Developments'. The fill placement methodology for the works involved:

- preparing the base by stripping all loose surficial fill, topsoil, soft material, vegetation, and materials containing significant organic matter to expose the natural soil subgrade
- sorting and mixing the fill materials to eliminate oversize particles greater than 20 % by volume, no particles coarser than 37.5 mm, and no particle over 200 mm in any dimension
- placing approved fill material in loose horizontal layers not exceeding 250 mm in thickness
- compacting the controlled fill materials to achieve a target dry density ratio of not less than 95 % Standard Compaction (AS 1289: 5.1.1, 5.4.1 or 5.7.1)
- moisture-conditioning the fill to within 85 % – 115 % of the standard optimum moisture content (SOMC)
- completing field density testing at a frequency for large scale developments (Type 1 AS3798) which nominates a frequency of not less than:
 - one test per layer or 200 mm per 2500 m²
 - one test per 500 m³ distributed reasonably evenly throughout the full depth and area, or
 - three tests per site visit; whichever requires the most tests.

3. INSPECTION AND TESTING

3.1 SUBGRADE PREPARATION

Site stripping was carried out during the initial stages of the project and presented to the on-site GITA for inspection. The stripping was conducted to expose suitable subgrade material which involved the removal of all surface vegetation and topsoil.

The subgrade was visually assessed using tactile methods described in AS1726 (2017) and approved by the GITA representative. Typically, the subgrade material comprised silty CLAY (CI- CH), medium to high plasticity, brown, and was found to be dry and in a stiff or better consistency. The exposed subgrade was considered suitable and approved for subsequent fill placement. The subgrade soil was then ripped and moisture conditioned prior to the placement of subsequent fill layers.

3.2 CONSTRUCTION MATERIALS

The fill material used in this project was nominated by the on-site contractor and sourced from on-site excavations.

The material was carted to the site and stockpiled adjacent to the fill zones. Ground Science performed an assessment of the fill source to identify the following material characteristics:

- material suitability as an engineering property
- cohesiveness
- free from building debris and vegetative matter
- oversize rock particles.

Visual assessments on the above-mentioned properties were conducted on-site and the fill material used was considered acceptable for use on this project. The nominated fill products were visually assessed to comprise silty CLAY(CI-CH), medium to high plasticity, and brown. The moisture content was observed to be dry of the SOMC.

Ground Science did not perform any chemical or environmental analysis of the above fill sources. Fill materials that were found to be dry were moisture conditioned using a water cart prior to and during placement. All fill materials hauled to the site were however generally considered suitable for use as engineered fill.

3.3 FILL CONSTRUCTION

The contractor had the following plant-available onsite during the construction period for use in the fill placement:

- padfoot roller
- highway truck
- excavator
- water cart
- dozer.

During fill placement, the weather conditions were generally fine to overcast with intermittent windy conditions and occasional drizzle.

The filling process was generally consistent throughout the project and involved the approved fill sources stockpiled adjacent to the fill placement zones. The material was spread using an on-site dozer into thin loose layers and moisture conditioned. Each layer was compacted using a Padfoot Roller applying a minimum of 6

passes, per layer observed. The thin layers of fill were compacted to form a composite layer of up to a maximum of 200 mm thick, prior to undertaking the field density testing.

Throughout the filling process and/or at the completion of the day's production, compaction testing was performed to assess the achieved density ratio of each layer. **Appendix A** provides a guide to the fill placement and is limited to the areas described in this report. It is considered that a 100 mm to 150 mm thick layer of topsoil may be spread at the completion of all works, which does not form part of the Level 1 process. Any fill placed as part of newly constructed drainage, sewer works, or similar does not form part of this Level 1 report.

3.4 RESULTS OF COMPACTION CONTROL TESTING

Level 1 Inspection and Testing was undertaken by an experienced technician from Ground Science who attended the site for the duration of the construction phase and nominated the location of the in-situ density tests. All laboratory testing was undertaken in our NATA-accredited Thomastown laboratory.

Testing comprised a total of 7 in-situ density tests using a nuclear moisture-density gauge in accordance with Australian Standard (AS1289.5.8.1) with 7 "Rapid HILF" Compaction tests (AS1289.5.7.1) of 95% standard compaction.

A summary of the field density tests performed for the project is presented in **Appendix A**. Field density and compaction control testing report sheets are presented in **Appendix B**. It should be noted that the tests are a representation of the fill placed and support the visual assessment of the works completed.

Test #2, #3 and #4 failed to meet the required target density ratio and the area of these tests was subsequently reworked, recompacted, and retested. All the re-tested areas achieved compliant test results. The following test numbers correspond to the re-tested locations of the failed areas:

- test #2 – re-tested #8
- test #3 – re-tested #9
- test #4 – re-tested #10.

All other tests achieved the target density ratio of 95% standard compaction. The moisture ratio of the compacted fill material was found to be within the recommended moisture ratio.

3.5 FINAL SURFACE LEVELS

Observations were made by a Ground Science staff member that filling had been completely up to the nominated finished levels as per confirmation provided from the contractor's site foreman. The observed final levels are the constructed finished surface levels of the controlled fill. It should be noted that the overall fill depths are estimated using onsite visual tactile methods and may not be a true representation of fill depths given that conditions onsite may change over time. True fill depths should be obtained from the contractor's survey data.

4. COMPLIANCE

Ground Science Staff have undertaken Level 1 Inspection and Testing Services of the construction of the controlled fill in the areas designated in **Appendix A**. Ground Science field staff have also observed that the prepared subgrade provided an adequate base for the subsequent placement of controlled fill.

Based on observations made by Ground Science staff and the results of density tests, we consider that the controlled fill placed has been constructed in accordance with the guidelines provided by AS3798 (2007) and AS2870 (2011).

It should be noted that the final fill layers may be subjected to adverse weather conditions resulting in either surface softening or drying and cracking over time; regardless of the compactive efforts and moisture conditioning applied during the works. The integrity of the top 200mm to 300mm of the fill will deteriorate with

time and should be taken into account by the foundation engineer prior to the construction of dwellings or buildings. The levels nominated in this report are a guide to the amounts of fill placed and do not necessarily reflect an accurate survey of the fill levels.

5. UNDERSTANDING LEVEL 1 INSPECTION & TESTING

The purpose of performing Level 1 Inspection and Testing is to ensure compliance of the fill with the specification. The engagement of a Geotechnical Inspection Testing Authority (GITA) allows the contractor to perform their role in the construction of the filling operation while the GITA monitors the quality control process of the fill placement. The visual observations of thorough processes and work practices by the contractor allows the GITA to approve the subsequent placement of fill without having to wait for the completion of testing and the extended time it takes to get a test result back. The GITA will however, carry out random spot checks of the filling operations throughout the day's production as confirmation that the placement procedures and the fill moisture content is appropriate. At the end of a day's production the GITA will sign off the completed works as satisfactory. Any failed tests will result in that particular area of operation requiring rectification in the following mornings activities. This may be as simple as extra rolling with compaction plant if moisture conditioning is suitable. Sometimes these areas may be retested if the GITA feels it is necessary.

While AS3798 (2007) is a guideline on the minimum requirements of filling on commercial and residential developments, some projects require a more detailed project specification to deal with site specific issues. While moisture conditioning of fill sources aids in the ease with which compaction is achieved, it is not necessarily a physical characteristic that determines if the placed fill is acceptable. In some situations, the moisture requirement is an extremely important function of the final constructed product. In these situations, a specific project specification should apply to the project as detailed by the designing geotechnical engineer. These are typical of clay liners for wet lands, dams, landfill liners and caps and an array of other engineering situations. Creating a consolidated platform of which is similar to equivalent surrounding natural conditions is the primary aim of level one processes, preventing the occurrence of differential ground movements to footing structures.

Level 1 Inspection & Testing requires full time inspection and testing of the fill placement undertaken on a site. Ground Science (project GITA), are notified daily (or at the completion of each day's work) by the project foreman where subsequent days of fill placement under Level 1 is to occur. On projects that rely upon the importation of a fill source, there can be delays in the receipt of sufficient materials to warrant fill placement works which may result in periods of time where a GITA representative is not required on site. It is the contractor's responsibility to notify the GITA when works proceed and their attendance on site is required again. A GITA relies upon the integrity of the contractor to advise when site attendance is required and makes all reasonable visual attempts to assess if the works are the same as the previous days attendance.



6. LIMITATIONS

This type of investigation (as per our commission) is not designed or capable of locating all soil conditions, (which can vary even over short distances). The advice given in this report is based on the assumption that the test results are representative of the overall soil conditions. However, it should be noted that actual conditions in some parts of the Site might differ from those found. If further sampling reveals soil conditions significantly different from those shown in our findings, Ground Science must be consulted. Maintenance and upkeep of finished fill placement must be regularly monitored as exposure to extended weather periods/other elements may cause surface drying which may lead to cracking. Conversely, excessive exposure to moisture may cause heaving/softening in the soils.

It is recognised that the passage of time affects the information and assessment provided in this document. Ground Science's assessment is based on information that existed at the time of the preparation of this document. It is understood that the services provided allowed Ground Science to form no more than an opinion of the actual site conditions observed during sampling and observations of the site visit and cannot be used to assess the effects of any subsequent changes in the quality of the site, or its surroundings, or any laws or regulations.

The scope and the period of Ground Science services are described in the proposal and are subject to restrictions and limitations. Ground Science did not perform a complete assessment of all possible conditions or circumstances that may exist at the Site. If a service is not expressly indicated, do not assume it has been provided. If a matter is not addressed, do not assume that any determination has been made by Ground Science in regards to it.

Where data has been supplied by the client or a third party, it is assumed that the information is correct unless otherwise stated. No responsibility is accepted by Ground Science for incomplete or inaccurate data supplied by others.

Any drawings or figures presented in this report should be considered only as pictorial evidence of our work. Therefore, unless otherwise stated, any dimensions should not be used for accurate calculations or dimensioning.

This document is COPYRIGHT- all rights reserved. No part of this document may be reproduced or copied in any form or by means without written permission by Ground Science Pty Ltd. All other property in this submission shall not pass until all fees for preparation have been settled. This submission is for the use only of the party to whom it is addressed and for no other purpose. No responsibility is accepted to any third party who may use or rely on the whole or any part of the content of this submission. No responsibility will be taken for this report if it is altered in any way, or not reproduced in full. This document remains the property of Ground Science Pty Ltd until all fees and monies have been paid in full.



7. REFERENCES

- AS3798 (2007) Guidelines on Earthworks for Residential and Commercial Developments.
- AS1289 Methods of Testing Soils for Engineering Purposes.
- AS1726 (2017): Geotechnical Site Investigations

APPENDIX A

Field Density Test Summary and Test Locations

Project Summary Report



Report Date: 27/07/2022
Client: BildGroup
7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061
Contact: Jamie Lancaster
Project Number: GS6240/1
Project Name: Lucas Estate - Stage K1-K2 (Level 1)
Project Location: Ballarat
Specification: 95% Standard Compaction & +/- 3% Moisture Variation
Test Methods: AS 1289 5.7.1 STD & 5.8.1 & 2.1.1

Ground Science Pty Ltd
Ground Science Laboratory
13 Brock Street Thomastown Victoria 3074
Phone: (03) 9464 4617
Email: chris@groundscience.com.au

Lot #	Sample #	Date Sampled	Location	Easting	Northing	Elevation (m)	Layer	Relative Compaction (%)	Moisture Variation (%)	Moisture Content (%)	Field Wet Density (t/m3)
**	62401-S1	10/03/2022	From n/w corner of lot 1935	13m east	9m south	**	1	95.5	-0.5	20.7	2.03
**	62401-S2	10/03/2022	From n/w corner of lot 1936	15m east	7m south	**	1	93.0	0.5	18.5	1.97
**	62401-S3	10/03/2022	From n/w corner of lot 1937	20m east	6m south	**	1	92.5	0.5	11.4	2.07
**	62401-S4	10/03/2022	From n/w corner of lot 1938	21m east	6m south	**	1	91.0	2.0	15.6	1.84

Moisture Variation Note:

Positive values = test is dry of OMC

Negative values = test is wet of OMC

Project Summary Report



Report Date: 27/07/2022
Client: BildGroup
7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061
Contact: Jamie Lancaster
Project Number: GS6240/1
Project Name: Lucas Estate - Stage K1-K2 (Level 1)
Project Location: Ballarat
Specification: 95% Standard Compaction & +/- 3% Moisture Variation
Test Methods: AS 1289 5.7.1 STD & 5.8.1 & 2.1.1

Ground Science Pty Ltd
Ground Science Laboratory
13 Brock Street Thomastown Victoria 3074
Phone: (03) 9464 4617
Email: chris@groundscience.com.au

Lot #	Sample #	Date Sampled	Location	Location		Elevation (m)	Layer	Relative Compaction (%)	Moisture Variation (%)	Moisture Content (%)	Field Wet Density (t/m3)
**	62401-S8	02/06/2022	Retest of 2	**	**	**	1	100.0	-0.5	23.6	2.04
**	62401-S9	02/06/2022	Retest of 3	**	**	**	1	103.5	-1.0	28.8	2.03
**	62401-S10	02/06/2022	Retest of 4	**	**	**	1	103.0	-0.5	24.3	2.12

Moisture Variation Note:

Positive values = test is dry of OMC

Negative values = test is wet of OMC

Project Summary Report



Report Date: 27/07/2022
Client: BildGroup
7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061
Contact: Jamie Lancaster
Project Number: GS6240/1
Project Name: Lucas Estate - Stage K1-K2 (Level 1)
Project Location: Ballarat
Specification: 95% Standard Compaction & +/- 3% Moisture Variation
Test Methods: AS 1289 5.7.1 STD & 5.8.1 & 2.1.1

Ground Science Pty Ltd
Ground Science Laboratory
13 Brock Street Thomastown Victoria 3074
Phone: (03) 9464 4617
Email: chris@groundscience.com.au


Lot #	Sample #	Date Sampled	Location	Latitude	Longitude	Elevation (m)	Layer	Relative Compaction (%)	Moisture Variation (%)	Moisture Content (%)	Field Wet Density (t/m3)
**	62401-S16	21/07/2022	From N/E corner of lot 1940	15m S	7m W	**	1	101.0	-3.0	20.0	2.12
**	62401-S17	21/07/2022	From N/E corner of lot 1916	15m S	7m W	**	1	96.0	-3.0	19.6	2.11
**	62401-S18	21/07/2022	From N/E corner of lot 1917	15m S	7m W	**	1	98.0	-2.5	18.4	2.12
**	62401-S19	21/07/2022	From N/E corner of lot 1918	15m S	7m W	**	1	95.5	-3.0	27.3	2.12
**	62401-S20	21/07/2022	From N/E corner of lot 1919	15m S	7m W	**	1	105.5	-1.5	20.8	2.22
**	62401-S21	21/07/2022	From N/E corner of lot 1920	15m S	7m W	**	1	102.0	-2.0	19.2	2.21
**	62401-S22	21/07/2022	From N/E corner of lot 1921	15m S	7m W	**	1	101.0	-2.0	20.2	2.20
**	62401-S23	21/07/2022	From N/E corner of lot 1922	15m S	7m W	**	1	106.0	-1.5	22.7	2.20
**	62401-S24	21/07/2022	From N/E corner of lot 1923	15m S	7m W	**	1	104.0	-2.0	21.1	2.21
**	62401-S25	21/07/2022	From N/E corner of lot 1929	15m S	7m W	**	1	98.5	-2.0	23.4	2.12

Moisture Variation Note:

Positive values = test is dry of OMC

Negative values = test is wet of OMC

Sample Locations Plan

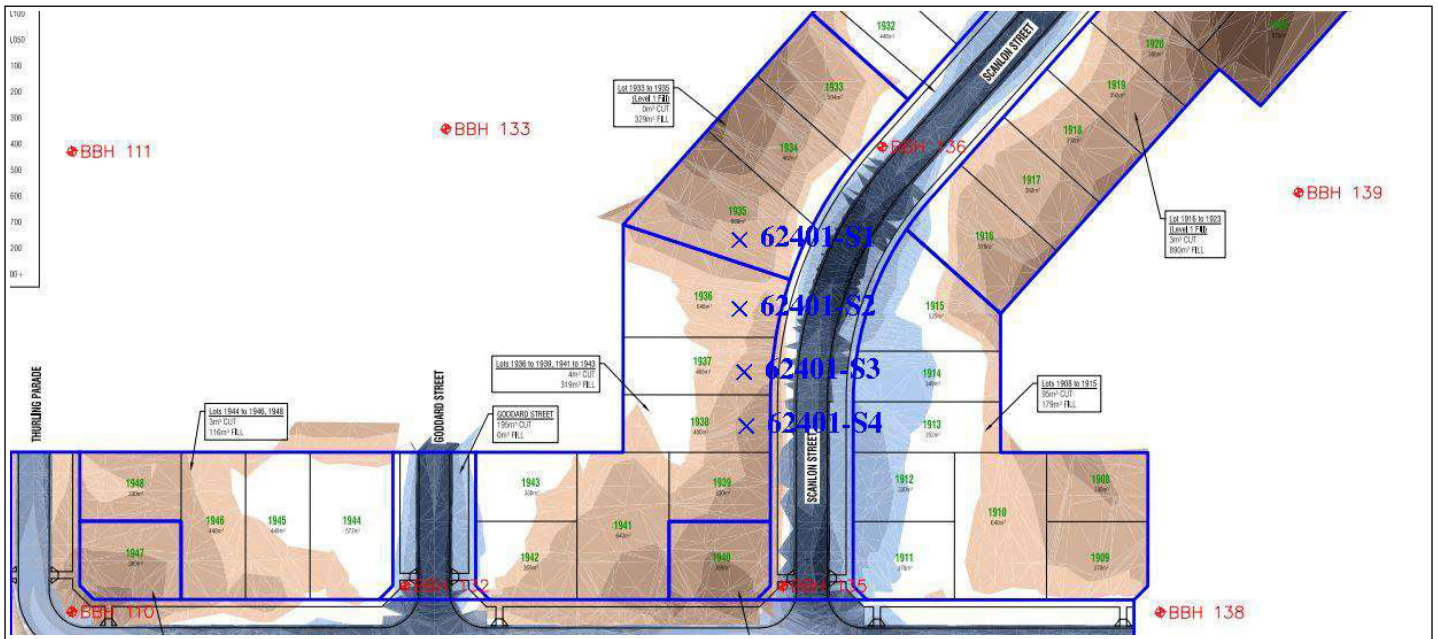

APPENDIX B

Field Density Test Report Sheets

Material Test Report



Report Number: GS6240/1-1A
Issue Number: 1
Date Issued: 20/07/2022
Client: BildGroup
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061
Contact: Ethan
Project Number: GS6240/1
Project Name: Lucas Estate - Stage K1-K2 (Level 1)
Project Location: Ballarat
Work Request: 7410
Date Sampled: 10/03/2022 10:30
Dates Tested: 10/03/2022 - 16/03/2022
Sampling Method: AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted
Specification: 95% Standard Compaction & +/- 3% Moisture Variation
Location: Ballarat
Material: silty CLAY, medium to high plasticity, brown, trace of gravel
Material Source: On-site

Ground Science Pty Ltd
 Ground Science Laboratory
 13 Brock Street Thomastown Victoria 3074
 Phone: (03) 9464 4617
 Email: brent@groundscience.com.au

Accredited for compliance with ISO/IEC 17025 - Testing



Brent Elliott

Approved Signatory: Brent Elliott
Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1				
Sample Number	62401-S1	62401-S2	62401-S3	62401-S4
Date Tested	10/03/2022	10/03/2022	10/03/2022	10/03/2022
Time Tested	12:27	12:32	12:36	12:41
Test Request #/Location	From n/w corner of lot 1935	From n/w corner of lot 1936	From n/w corner of lot 1937	From n/w corner of lot 1938
Easting	13m east	15m east	20m east	21m east
Northing	9m south	7m south	6m south	6m south
Layer / Reduced Level	1	1	1	1
Thickness of Layer (mm)	200	200	200	200
Soil Description	Silty CLAY, m-h plas, brown, trace of gravel	Silty CLAY, m-h plas, brown, trace of gravel	Gravelly CLAY, medium to high plasticity, brown	Silty CLAY, m-h plas, brown, trace of gravel
Test Depth (mm)	175	175	175	175
Sieve used to determine oversize (mm)	19.0	19.0	19.0	19.0
Percentage of Wet Oversize (%)	0	0	1	0
Field Wet Density (FWD) t/m ³	2.03	1.97	2.07	1.84
Field Moisture Content %	20.7	18.5	11.4	15.6
Field Dry Density (FDD) t/m ³	1.68	1.66	1.86	1.59
Peak Converted Wet Density t/m ³	2.12	2.12	**	2.02
Adjusted Peak Converted Wet Density t/m ³	**	**	2.24	**
Moisture Variation (Wv) %	-0.5	0.5	**	2.0
Adjusted Moisture Variation %	**	**	0.5	**
Hilf Density Ratio (%)	95.5	93.0	92.5	91.0
Compaction Method	Standard	Standard	Standard	Standard
Report Remarks	**	**	**	**

Moisture Variation Note:

Positive values = test is dry of OMC
 Negative values = test is wet of OMC

Material Test Report



Report Number: GS6240/1-3A
Issue Number: 2 - This version supersedes all previous issues
Reissue Reason: Stages separated
Date Issued: 27/07/2022
Client: BildGroup
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061
Contact: Jamie Lancaster
Project Number: GS6240/1
Project Name: Lucas Estate - Stage K1-K2 (Level 1)
Project Location: Ballarat
Work Request: 8673
Date Sampled: 02/06/2022 11:30
Dates Tested: 02/06/2022 - 06/06/2022
Sampling Method: AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted
Specification: 95% Standard Compaction & +/- 3% Moisture Variation
Location: Ballarat
Material: Silty CLAY, medium to high plasticity, brown

Ground Science Pty Ltd
 Ground Science Laboratory
 13 Brock Street Thomastown Victoria 3074
 Phone: (03) 9464 4617
 Email: brent@groundscience.com.au

Accredited for compliance with ISO/IEC 17025 - Testing



Brent Elliott

Approved Signatory: Brent Elliott
Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1			
Sample Number	62401-S8	62401-S9	62401-S10
Date Tested	02/06/2022	02/06/2022	02/06/2022
Time Tested	11:51	12:02	12:19
Test Request #/Location	Retest of 2	Retest of 3	Retest of 4
Layer / Reduced Level	1	1	1
Thickness of Layer (mm)	200	200	200
Soil Description	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown
Test Depth (mm)	175	175	175
Sieve used to determine oversize (mm)	19.0	19.0	19.0
Percentage of Wet Oversize (%)	4	0	7
Field Wet Density (FWD) t/m ³	2.04	2.03	2.12
Field Moisture Content %	23.6	28.8	24.3
Field Dry Density (FDD) t/m ³	1.65	1.57	1.71
Peak Converted Wet Density t/m ³	**	1.96	**
Adjusted Peak Converted Wet Density t/m ³	2.04	**	2.06
Moisture Variation (Wv) %	**	-1.0	**
Adjusted Moisture Variation %	-0.5	**	-0.5
Hilf Density Ratio (%)	100.0	103.5	103.0
Compaction Method	Standard	Standard	Standard
Report Remarks	**	**	**

Moisture Variation Note:

Positive values = test is dry of OMC
 Negative values = test is wet of OMC

Material Test Report



Report Number: GS6240/1-6
Issue Number: 1
Date Issued: 27/07/2022
Client: BildGroup
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061
Contact: Jamie Lancaster
Project Number: GS6240/1
Project Name: Lucas Estate - Stage K1-K2 (Level 1)
Project Location: Ballarat
Work Request: 9409
Date Sampled: 21/07/2022 9:45
Dates Tested: 21/07/2022 - 26/07/2022
Sampling Method: AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted
Specification: 95% Standard Compaction & +/- 3% Moisture Variation
Location: lucas
Material: Silty CLAY, medium to high plasticity, brown
Material Source: onsite

Ground Science Pty Ltd
 Ground Science Laboratory
 13 Brock Street Thomastown Victoria 3074
 Phone: (03) 9464 4617
 Email: brent@groundscience.com.au

Accredited for compliance with ISO/IEC 17025 - Testing



Brent Elliott

Approved Signatory: Brent Elliott
Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1					
Sample Number	62401-S16	62401-S17	62401-S18	62401-S19	62401-S20
Date Tested	21/07/2022	21/07/2022	21/07/2022	21/07/2022	21/07/2022
Time Tested	09:30	09:45	10:10	10:30	10:45
Test Request #/Location	From N/E corner of lot 1940	From N/E corner of lot 1916	From N/E corner of lot 1917	From N/E corner of lot 1918	From N/E corner of lot 1919
Latitude	15m S	15m S	15m S	15m S	15m S
Longitude	7m W	7m W	7m W	7m W	7m W
Layer / Reduced Level	1	1	1	1	1
Thickness of Layer (mm)	300	300	300	300	300
Soil Description	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown
Test Depth (mm)	275	275	275	275	275
Sieve used to determine oversize (mm)	19.0	19.0	19.0	19.0	19.0
Percentage of Wet Oversize (%)	0	3	1	1	3
Field Wet Density (FWD) t/m ³	2.12	2.11	2.12	2.12	2.22
Field Moisture Content %	20.0	19.6	18.4	27.3	20.8
Field Dry Density (FDD) t/m ³	1.77	1.77	1.79	1.67	1.84
Peak Converted Wet Density t/m ³	2.10	**	**	**	**
Adjusted Peak Converted Wet Density t/m ³	**	2.20	2.15	2.22	2.10
Moisture Variation (Wv) %	-3.0	**	**	**	**
Adjusted Moisture Variation %	**	-3.0	-2.5	-3.0	-1.5
Hilf Density Ratio (%)	101.0	96.0	98.0	95.5	105.5
Compaction Method	Standard	Standard	Standard	Standard	Standard
Report Remarks	**	**	**	**	**

Moisture Variation Note:

Positive values = test is dry of OMC
 Negative values = test is wet of OMC

Material Test Report



Report Number: GS6240/1-6
Issue Number: 1
Date Issued: 27/07/2022
Client: BildGroup
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061
Contact: Jamie Lancaster
Project Number: GS6240/1
Project Name: Lucas Estate - Stage K1-K2 (Level 1)
Project Location: Ballarat
Work Request: 9409
Date Sampled: 21/07/2022 9:45
Dates Tested: 21/07/2022 - 26/07/2022
Sampling Method: AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted
Specification: 95% Standard Compaction & +/- 3% Moisture Variation
Location: lucas
Material: Silty CLAY, medium to high plasticity, brown
Material Source: onsite

Ground Science Pty Ltd
 Ground Science Laboratory
 13 Brock Street Thomastown Victoria 3074
 Phone: (03) 9464 4617
 Email: brent@groundscience.com.au

Accredited for compliance with ISO/IEC 17025 - Testing



Brent Elliott

Approved Signatory: Brent Elliott

Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1					
Sample Number	62401-S21	62401-S22	62401-S23	62401-S24	62401-S25
Date Tested	21/07/2022	21/07/2022	21/07/2022	21/07/2022	21/07/2022
Time Tested	11:00	11:15	11:30	11:55	12:15
Test Request #/Location	From N/E corner of lot 1920	From N/E corner of lot 1921	From N/E corner of lot 1922	From N/E corner of lot 1923	From N/E corner of lot 1929
Latitude	15m S	15m S	15m S	15m S	15m S
Longitude	7m W	7m W	7m W	7m W	7m W
Layer / Reduced Level	1	1	1	1	1
Thickness of Layer (mm)	300	300	300	300	300
Soil Description	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown	Silty CLAY, m-h plas, brown
Test Depth (mm)	275	275	275	275	275
Sieve used to determine oversize (mm)	19.0	19.0	19.0	19.0	19.0
Percentage of Wet Oversize (%)	2	4	3	1	4
Field Wet Density (FWD) t/m ³	2.21	2.20	2.20	2.21	2.12
Field Moisture Content %	19.2	20.2	22.7	21.1	23.4
Field Dry Density (FDD) t/m ³	1.86	1.83	1.79	1.82	1.72
Peak Converted Wet Density t/m ³	**	**	**	**	**
Adjusted Peak Converted Wet Density t/m ³	2.16	2.18	2.07	2.12	2.15
Moisture Variation (Wv) %	**	**	**	**	**
Adjusted Moisture Variation %	-2.0	-2.0	-1.5	-2.0	-2.0
Hilf Density Ratio (%)	102.0	101.0	106.0	104.0	98.5
Compaction Method	Standard	Standard	Standard	Standard	Standard
Report Remarks	**	**	**	**	**

Moisture Variation Note:

Positive values = test is dry of OMC

Negative values = test is wet of OMC

APPENDIX C

Site Photographs



2 Jun 2022 at 11:44:45 am
Reworking failed area



2 Jun 2022 at 11:44:27 am
Reworking failed area

