

**ABN 31 105 704 078**

13 Brock Street, Thomastown

Victoria 3074

(P) +61 3 9464 4617

(F) +61 3 9464 4618



# **LEVEL 1 INSPECTION & TESTING LUCAS GRANGE ESTATE - STAGE 2F**

Prepared for Bild Group

**Report Reference: GS6110.1 AB**

**Date: 20 May 2022**

**ABN 31 105 704 078**

13 Brock Street, Thomastown

Victoria 3074

(P) +61 3 9464 4617

(F) +61 3 9464 4618



## PROJECT DETAILS

Project Reference	GS6110.1	Rev	AB
Project Title	Lucas Grange Estate Stage 2F		
Project Location	Alfredton, Ballarat	State	VIC
Date	20 May 2022		

## CLIENT DETAILS

Prepared For (Client)	Bild Group
Client Address	133 Metrolink Circuit, Campbellfield VIC 3061

## DISTRIBUTION

Original Held By	Ground Science Pty Ltd
One (1) Electronic Copy	Bild Group

This document presents the results of the Level 1 Inspection and Testing performed by Ground Science for the aforementioned project, as the nominated project Geotechnical Inspection & Testing Authority (GITA). This report is detailed for the sole use of the intended recipient(s). Should you have any questions related to this report please do not hesitate to contact the undersigned.

### AUTHOR:

**Anton Manoj**  
Geotechnical Engineer

### REVIEWED:

**Gee Singh, MIEAust (NER)**  
Senior Geotechnical Engineer

# Table of Contents

---

1. INTRODUCTION .....	1
2. SCOPE OF WORK.....	1
2.1 AREAS OF WORK.....	1
2.2 PLACEMENT METHODOLOGY .....	1
3. INSPECTION AND TESTING .....	1
3.1 SUBGRADE PREPARATION.....	1
3.2 CONSTRUCTION MATERIALS .....	2
3.3 FILL CONSTRUCTION .....	2
3.4 RESULTS OF COMPACTION CONTROL TESTING.....	3
3.5 FINAL SURFACE LEVELS .....	3
4. COMPLIANCE .....	3
5. UNDERSTANDING LEVEL 1 INSPECTION & TESTING .....	3
6. LIMITATIONS.....	5
7. REFERENCES .....	6

## **APPENDICES**

APPENDIX A	FIELD DENSITY TEST SUMMARY SHEETS
APPENDIX B	FIELD DENSITY TEST REPORT SHEETS
APPENDIX C	SITE PHOTOGRAPHS

## 1. INTRODUCTION

This report presents the results of the inspection activities, compaction control and laboratory testing services performed by Ground Science Pty Ltd for the development at Lucas Grange Estate Stage 2F, Alfredton, Ballarat, Victoria (the site).

Ground Science were engaged to provide Level 1 Inspection and Testing services for the construction of building platforms to support proposed residential allotments, as part of the bulk earthworks phase of the project. Authorisation to proceed was provided by Bild Group (the 'Client').

Level 1 Testing as defined in AS3798 (2007) 'Guidelines on Earthworks for Commercial and Residential Developments' provides for full time inspection of the construction of controlled fill and compaction testing in accordance with AS1289 'Methods of Testing Soils for Engineering Purposes'. The Level 1 Inspection and Testing services described in this report were undertaken by experienced geotechnicians from Ground Science.

## 2. SCOPE OF WORK

### 2.1 AREAS OF WORK

The areas requiring Level 1 Inspection & Testing are shown in Appendix A, which is based on plans prepared by Integra (LUG2F-CD-710 REV 1). This report details the Level 1 earthwork process performed onsite which commenced on the 21<sup>st</sup> December 2021 and was completed on the 18<sup>th</sup> January 2022, including 3 full day of filling operations.

### 2.2 PLACEMENT METHODOLOGY

The placement of controlled fill on the above-mentioned areas was carried out in accordance with Level 1 fill procedures as detailed in AS3798 (2007) 'Guidelines on Earthworks for Commercial and Residential Developments'. The following fill placement guideline was adopted for the works:

- All topsoil and vegetation were removed to expose the natural soil subgrade;
- Suitable fill material, sourced by the contractor and approved by Ground Science, was placed in loose horizontal layers not exceeding 150mm in thickness;
- The controlled fill material was compacted to achieve a target Dry Density Ratio of at least 95% Standard Compaction (AS 1289: 5.1.1, 5.4.1 or 5.7.1), based on the sites proposed use for residential purposes;
- The fill was moisture conditioned to within 85% – 115% of the standard optimum moisture content;
- The fill material was sorted and mixed to remove particles greater than 20% by volume, particles coarser than 37.5mm and no particle over 100mm in any dimension;
- The frequency of field density testing adopted for the project was generally in line with the requirements for large scale developments (Type 1), as detailed in AS3798 (2007), which nominates a frequency of not less than:
  - 1 test per layer or 200mm per 2500m<sup>2</sup>;
  - 1 test per 500m<sup>3</sup> distributed reasonably evenly throughout the full depth and area; or
  - 3 tests per site visit; whichever requires the most tests.

## 3. INSPECTION AND TESTING

### 3.1 SUBGRADE PREPARATION

Site stripping was carried out during the initial stages of the project and presented to the onsite GITA for inspection. It is understood that stripping was conducted to expose suitable subgrade material which involved the removal of

all surface vegetation, and topsoil and then proof rolled with a fully loaded Moxy truck with a few soft spots observed. Observed soft spots were excavated until a suitable subgrade material is present.

The above subgrade was visually assessed using tactile methods described in AS1726 (2017) and approved by the GITA representative throughout the project. Typically, the subgrade material comprises silty CLAY (CI- CH), medium to high plasticity, brown, and was found to be dry and in a stiff or better consistency. The exposed subgrade was considered suitable and approved for subsequent fill placement. Subgrade soil was then ripped, moisture conditioned, prior to the placement of the fill layers.

### 3.2 CONSTRUCTION MATERIALS

The fill material used in this project was nominated by the on-site contractor. The nominated fill used for the project was sourced from onsite excavations.

The material was carted to the site and stockpiled adjacent to the fill zones. Ground Science performed an assessment of the fill source to identify the following material characteristics:

- Material suitability as an engineering property;
- Cohesiveness;
- Free of building debris and vegetative matter;
- Free of oversize rock particles.

Visual assessments on the above-mentioned properties were conducted on-site and the fill material used was considered acceptable for use on this project. The nominated fill products were visually assessed to comprise of silty CLAY(CI-CH), medium to high plasticity, brown. The moisture content was observed to be dry of the optimum moisture content (OMC).

Ground Science did not perform any chemical or environmental analysis of the above fill sources. Fill materials that were found to be dry were moisture conditioned using a water cart prior to and during placement. All fill materials hauled to the site were however generally considered suitable for use as engineered fill.

### 3.3 FILL CONSTRUCTION

The contractor had the following plant available onsite during the construction period for use in the fill placement;

- Padfoot Roller;
- Excavator;
- Moxy Truck;
- Water Cart;
- Dozer.

During fill placement, the weather conditions were generally fine to overcast.

The filling process was generally consistent throughout the project and involved the approved fill sources stockpiled adjacent to the fill placement zones. The material was spread using an on-site dozer into thin loose layers and moisture conditioned. Each layer was compacted using a Padfoot Roller applying a minimum of 8 passes, per layer observed. The thin layers of fill were compacted to form a composite layer of up to a maximum of 200mm thick, prior to undertaking the field density testing. Generally, up to 4 layers were placed and compacted. The compacted fill was ripped, and moisture conditioned prior to the application of subsequent layers of fill. This process was adopted for the fill placement works.

Throughout the filling process and/or at the completion of the day's production, compaction testing was performed to assess the achieved density ratio of each layer. Appendix A provides a guide to the fill placement and is limited to the areas described in this report. It is considered that a 100mm to 150mm thick layer of topsoil may be spread at the completion of all works, which does not form part of the Level 1 process. Any fill placed as part of newly constructed drainage, sewer works, or similar does not form part of this Level 1 report.

### **3.4 RESULTS OF COMPACTION CONTROL TESTING**

Level 1 Inspection and Testing was undertaken by experienced technicians from Ground Science who attended the site for the duration of the construction phase and nominated the location of the in-situ density tests. Testing comprised a total of 15 in-situ density tests using a nuclear moisture-density gauge in accordance with Australian Standard (AS1289 5.8.1) and 15 "Rapid HILF" Compaction tests (AS1289 5.7.1).

A summary of the field density tests performed for the project is presented in Appendix A. Field density and compaction control testing report sheets are presented in Appendix B. It should be noted that the tests are a representation of the fill placed and support the visual assessment of the works completed.

Test #5 failed to achieve the target moisture ratio, hence, reworked and recompacted for a compliant test result is achieved.

All the tests achieved the target density ratio of 95% standard compaction. The moisture ratio of the compacted fill material was found to be within the recommended moisture ratio.

### **3.5 FINAL SURFACE LEVELS**

Observations were made by a Ground Science staff member that filling had been completely up to the nominated finished levels as per confirmation provided from the contractor's site foreman. The observed final levels are the constructed finished surface levels of the controlled fill. It should be noted that the overall fill depths are estimated using onsite visual tactile methods and may not be a true representation of fill depths given that conditions onsite may change over time. True fill depths should be obtained from the contractor's survey data.

## **4. COMPLIANCE**

Ground Science Staff have undertaken Level 1 Inspection and Testing Services of the construction of the controlled fill in the areas designated in Appendix A. Ground Science field staff have also observed that the prepared subgrade provided an adequate base for the subsequent placement of controlled fill.

Based on observations made by Ground Science staff and the results of density tests, we consider that the controlled fill placed has been constructed in accordance with the guidelines provided by AS3798 (2007) and AS2870 (2011).

It should be noted that the final fill layers may be subjected to adverse weather conditions resulting in either surface softening or drying and cracking over time; regardless of the compactive efforts and moisture conditioning applied during the works. The integrity of the top 200mm to 300mm of the fill will deteriorate with time and should be taken into account by the foundation engineer prior to the construction of dwellings or buildings. The levels nominated in this report are a guide to the amounts of fill placed and do not necessarily reflect an accurate survey of the fill levels.

## **5. UNDERSTANDING LEVEL 1 INSPECTION & TESTING**

The purpose of performing Level 1 Inspection and Testing is to ensure compliance of the fill with the specification. The engagement of a Geotechnical Inspection Testing Authority (GITA) allows the contractor to perform their role in the construction of the filling operation while the GITA monitors the quality control process of the fill placement. The visual observations of thorough processes and work practices by the contractor allows the GITA to approve the subsequent placement of fill without having to wait for the completion of testing and the extended time it takes



to get a test result back. The GITA will however, carry out random spot checks of the filling operations throughout the day's production as confirmation that the placement procedures and the fill moisture content is appropriate. At the end of a day's production the GITA will sign off the completed works as satisfactory. Any failed tests will result in that particular area of operation requiring rectification in the following mornings activities. This may be as simple as extra rolling with compaction plant if moisture conditioning is suitable. Sometimes these areas may be retested if the GITA feels it is necessary.

While AS3798 (2007) is a guideline on the minimum requirements of filling on commercial and residential developments, some projects require a more detailed project specification to deal with site specific issues. While moisture conditioning of fill sources aids in the ease with which compaction is achieved, it is not necessarily a physical characteristic that determines if the placed fill is acceptable. In some situations, the moisture requirement is an extremely important function of the final constructed product. In these situations, a specific project specification should apply to the project as detailed by the designing geotechnical engineer. These are typical of clay liners for wet lands, dams, landfill liners and caps and an array of other engineering situations. Creating a consolidated platform of which is similar to equivalent surrounding natural conditions is the primary aim of level one processes, preventing the occurrence of differential ground movements to footing structures.

Level 1 Inspection & Testing requires full time inspection and testing of the fill placement undertaken on a site. Ground Science (project GITA), are notified daily (or at the completion of each day's work) by the project foreman where subsequent days of fill placement under Level 1 is to occur. On projects that rely upon the importation of a fill source, there can be delays in the receipt of sufficient materials to warrant fill placement works which may result in periods of time where a GITA representative is not required on site. It is the contractor's responsibility to notify the GITA when works proceed and their attendance on site is required again. A GITA relies upon the integrity of the contractor to advise when site attendance is required and makes all reasonable visual attempts to assess if the works are the same as the previous days attendance.



## 6. LIMITATIONS

This type of investigation (as per our commission) is not designed or capable of locating all soil conditions, (which can vary even over short distances). The advice given in this report is based on the assumption that the test results are representative of the overall soil conditions. However, it should be noted that actual conditions in some parts of the Site might differ from those found. If further sampling reveals soil conditions significantly different from those shown in our findings, Ground Science must be consulted. Maintenance and upkeep of finished fill placement must be regularly monitored as exposure to extended weather periods/other elements may cause surface drying which may lead to cracking. Conversely, excessive exposure to moisture may cause heaving/softening in the soils.

It is recognised that the passage of time affects the information and assessment provided in this document. Ground Science's assessment is based on information that existed at the time of the preparation of this document. It is understood that the services provided allowed Ground Science to form no more than an opinion of the actual site conditions observed during sampling and observations of the site visit and cannot be used to assess the effects of any subsequent changes in the quality of the site, or its surroundings, or any laws or regulations.

The scope and the period of Ground Science services are described in the proposal and are subject to restrictions and limitations. Ground Science did not perform a complete assessment of all possible conditions or circumstances that may exist at the Site. If a service is not expressly indicated, do not assume it has been provided. If a matter is not addressed, do not assume that any determination has been made by Ground Science in regards to it.

Where data has been supplied by the client or a third party, it is assumed that the information is correct unless otherwise stated. No responsibility is accepted by Ground Science for incomplete or inaccurate data supplied by others.

Any drawings or figures presented in this report should be considered only as pictorial evidence of our work. Therefore, unless otherwise stated, any dimensions should not be used for accurate calculations or dimensioning.

This document is COPYRIGHT- all rights reserved. No part of this document may be reproduced or copied in any form or by means without written permission by Ground Science Pty Ltd. All other property in this submission shall not pass until all fees for preparation have been settled. This submission is for the use only of the party to whom it is addressed and for no other purpose. No responsibility is accepted to any third party who may use or rely on the whole or any part of the content of this submission. No responsibility will be taken for this report if it is altered in any way, or not reproduced in full. This document remains the property of Ground Science Pty Ltd until all fees and monies have been paid in full.





## 7. REFERENCES

- AS3798 (2007) Guidelines on Earthworks for Residential and Commercial Developments.
- AS1289 Methods of Testing Soils for Engineering Purposes.
- AS1726 (2017): Geotechnical Site Investigations

## **APPENDIX A**

### Field Density Test Summary

# Project Summary Report



**Report Date:** 20/05/2022  
**Client:** BildGroup  
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061  
**Contact:** Ben  
**Project Number:** GS6110/1  
**Project Name:** Lucas Grange Estate - Stage 2F (Level 1)  
**Project Location:** Ballarat  
**Specification:** 95% Standard Compaction & +/- 3% Moisture Variation  
**Test Methods:** AS 1289 5.7.1 STD & 5.8.1 & 2.1.1


Ground Science Pty Ltd  
 Ground Science Laboratory  
 13 Brock Street Thomastown Victoria 3074  
 Phone: (03) 9464 4617  
 Email: chris@groundscience.com.au


Lot #	Sample #	Date Sampled	Location	Latitude	Longitude	Elevation (m)	Layer	Relative Compaction (%)	Moisture Variation (%)	Moisture Content (%)	Field Wet Density (t/m3)
**	61101-S1	21/12/2021	From n/w corner of lot 223	5m south	10m east	**	1	108.5	2.0	21.1	2.12
**	61101-S2	21/12/2021	From n/w corner of lot 224	5m south	5m east	**	1	96.0	3.0	19.2	1.88
**	61101-S3	21/12/2021	From n/w corner of lot 224	5m south	10m east	**	1	97.5	3.0	20.6	1.91
**	61101-S4	14/01/2022	From SE corner of lot 223	2m S	5m W	**	1	105.0	3.0	19.7	2.04
**	61101-S5	14/01/2022	From SE corner of lot 223	12m S	7m W	**	1	103.0	4.5	18.1	1.99
**	61101-S6	14/01/2022	From SE corner of lot 224	5m S	6m W	**	1	99.0	3.0	20.3	1.94
**	61101-S7	18/01/2022	Retest of 5	**	**	**	1	97.0	0.0	23.2	1.93
**	61101-S8	18/01/2022	From s/w corner of lot 224	15m east	3m north	**	2	101.5	2.5	24.2	1.93
**	61101-S9	18/01/2022	From s/w corner of lot 223	7m east	3m north	**	3	100.5	2.5	22.6	1.89
**	61101-S10	18/01/2022	From s/w corner of lot 223	15m east	3m north	**	4	99.0	0.5	26.5	1.88
**	61101-S11	18/05/2022	From n/w corner of lot 236	5m south	3m east	**	1	103.5	0.5	19.7	2.14
**	61101-S12	18/05/2022	From n/w corner of lot 235	3m south	3m east	**	2	102.5	0.5	24.2	2.05
**	61101-S13	18/05/2022	From n/w corner of lot 234	5m south	3m east	**	3	99.5	-0.5	20.7	2.11
**	61101-S14	18/05/2022	From n/w corner of lot 213	3m south	25m east	**	2	101.0	3.0	28.7	1.84
**	61101-S15	18/05/2022	From n/w corner of lot 214	5m south	25m east	**	1	102.5	3.0	28.0	1.87

**Moisture Variation Note:**

Positive values = test is dry of OMC  
 Negative values = test is wet of OMC

# Sample Locations Plan

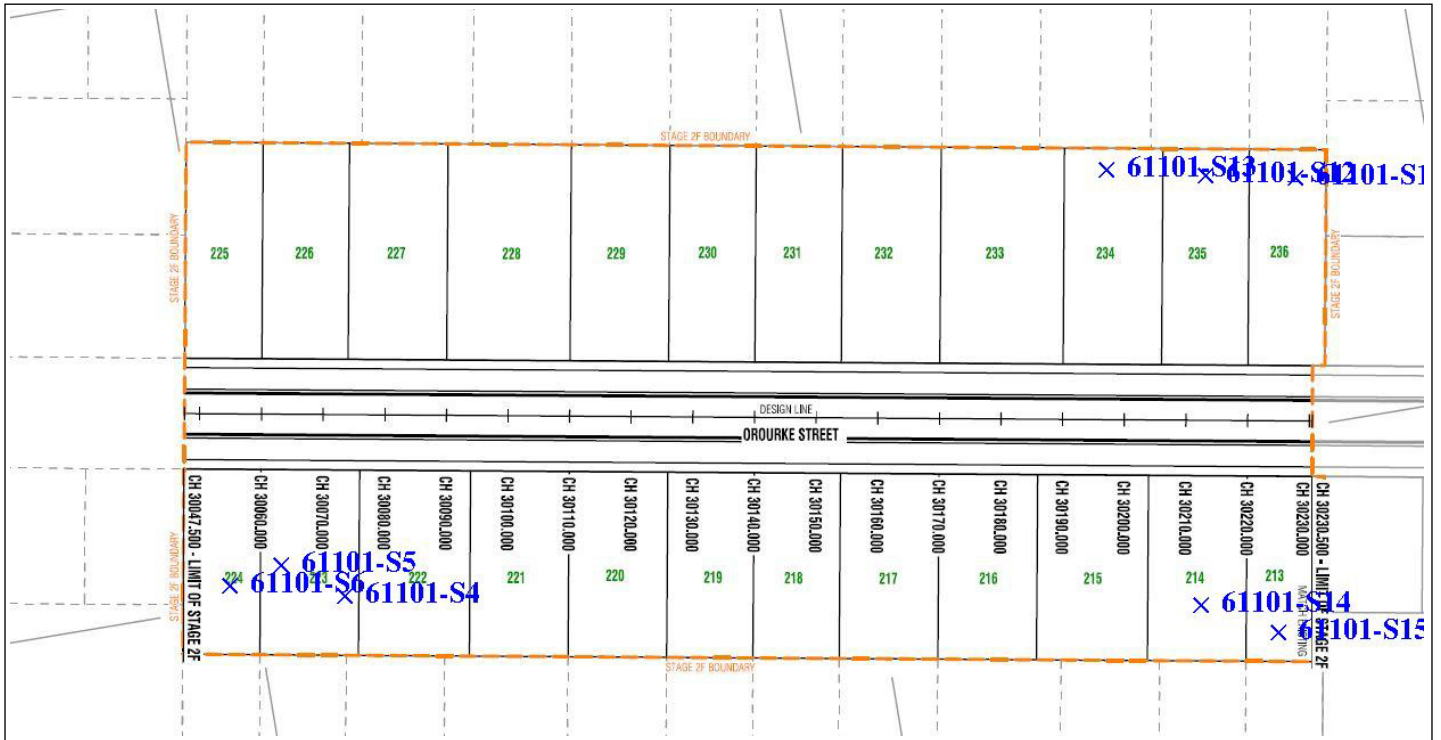

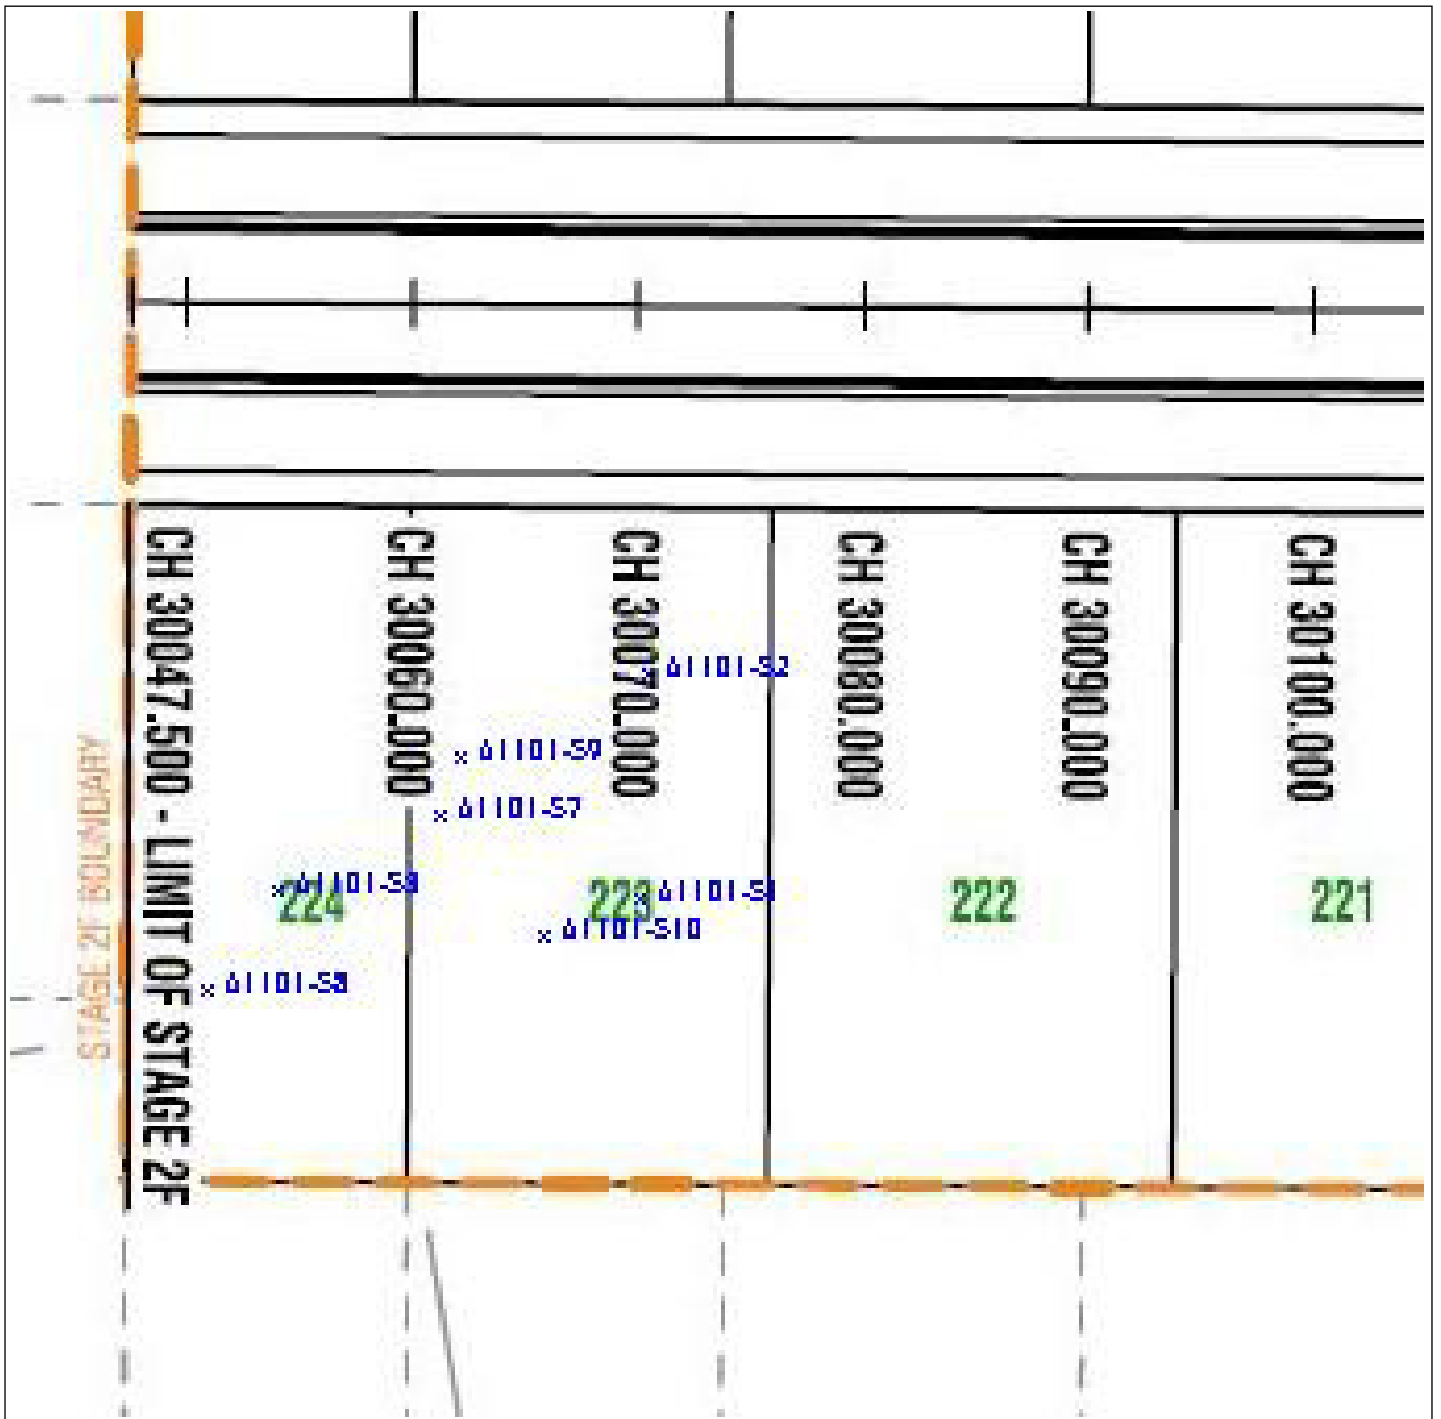

## **APPENDIX B**

Field Density Test Report Sheets

# Material Test Report



**Report Number:** GS6110/1-1  
**Issue Number:** 1  
**Date Issued:** 10/01/2022  
**Client:** BildGroup  
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061  
**Contact:** Sharon  
**Project Number:** GS6110/1  
**Project Name:** Lucas Grange Estate - Stage 2F (Level 1)  
**Project Location:** Ballarat  
**Work Request:** 6465  
**Date Sampled:** 21/12/2021 11:00  
**Dates Tested:** 21/12/2021 - 30/12/2021  
**Sampling Method:** AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted  
**Specification:** 95% Standard Compaction & +/- 3% Moisture Variation  
**Location:** Lucas Grange  
**Material:** Silty CLAY, medium to high plasticity, brown  
**Material Source:** On-site

Ground Science Pty Ltd  
 Ground Science Laboratory  
 13 Brock Street Thomastown Victoria 3074  
 Phone: (03) 9464 4617  
 Email: brent@groundscience.com.au

Accredited for compliance with ISO/IEC 17025 - Testing



*Brent Elliott*

Approved Signatory: Brent Elliott  
Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1			
Sample Number	61101-S1	61101-S2	61101-S3
Date Tested	21/12/2021	21/12/2021	21/12/2021
Time Tested	14:26	14:32	14:37
Test Request #/Location	From n/w corner of lot 223	From n/w corner of lot 224	From n/w corner of lot 224
Latitude	5m south	5m south	5m south
Longitude	10m east	5m east	10m east
Layer / Reduced Level	1	1	1
Thickness of Layer (mm)	150	150	150
Soil Description	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown
Test Depth (mm)	125	125	125
Sieve used to determine oversize (mm)	19.0	19.0	19.0
Percentage of Wet Oversize (%)	11	10	3
Field Wet Density (FWD) t/m <sup>3</sup>	2.12	1.88	1.91
Field Moisture Content %	21.1	19.2	20.6
Field Dry Density (FDD) t/m <sup>3</sup>	1.75	1.58	1.59
Peak Converted Wet Density t/m <sup>3</sup>	**	**	**
Adjusted Peak Converted Wet Density t/m <sup>3</sup>	1.96	1.96	1.96
Moisture Variation (Wv) %	**	**	**
Adjusted Moisture Variation %	2.0	3.0	3.0
Hilf Density Ratio (%)	<b>108.5</b>	<b>96.0</b>	<b>97.5</b>
Compaction Method	<b>Standard</b>	<b>Standard</b>	<b>Standard</b>
Report Remarks	**	**	**

**Moisture Variation Note:**

Positive values = test is dry of OMC  
 Negative values = test is wet of OMC

# Material Test Report




**Report Number:** GS6110/1-2  
**Issue Number:** 1  
**Date Issued:** 17/01/2022  
**Client:** BildGroup  
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061  
**Contact:** Sharon  
**Project Number:** GS6110/1  
**Project Name:** Lucas Grange Estate - Stage 2F (Level 1)  
**Project Location:** Ballarat  
**Work Request:** 6526  
**Dates Tested:** 14/01/2022 - 17/01/2022  
**Sampling Method:** AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted  
**Specification:** 95% Standard Compaction & +/- 3% Moisture Variation  
**Location:** Stage 2F Level 1  
**Material:** gravelly CLAY, medium to high plasticity, brown  
**Material Source:** Onsite

Ground Science Pty Ltd  
 Ground Science Laboratory  
 13 Brock Street Thomastown Victoria 3074  
 Phone: (03) 9464 4617  
 Email: tim@groundscience.com.au

Accredited for compliance with ISO/IEC 17025 - Testing



  
 Approved Signatory: Tim Senserrick  
 Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1			
Sample Number	61101-S4	61101-S5	61101-S6
Date Tested	14/01/2022	14/01/2022	14/01/2022
Time Tested	07:40	07:46	07:53
Test Request #/Location	From SE corner of lot 223	From SE corner of lot 223	From SE corner of lot 224
Line / Offset	2m S	12m S	5m S
Offset	5m W	7m W	6m W
Layer / Reduced Level	1	1	1
Thickness of Layer (mm)	200	200	200
Soil Description	Gravelly CLAY, medium to high plasticity, brown	**	**
Test Depth (mm)	175	175	175
Sieve used to determine oversize (mm)	19.0	19.0	19.0
Percentage of Wet Oversize (%)	2	9	5
Field Wet Density (FWD) t/m <sup>3</sup>	2.04	1.99	1.94
Field Moisture Content %	19.7	18.1	20.3
Field Dry Density (FDD) t/m <sup>3</sup>	1.71	1.68	1.61
Peak Converted Wet Density t/m <sup>3</sup>	**	**	**
Adjusted Peak Converted Wet Density t/m <sup>3</sup>	1.95	1.93	1.96
Moisture Variation (Wv) %	**	**	**
Adjusted Moisture Variation %	3.0	4.5	3.0
Hilf Density Ratio (%)	<b>105.0</b>	<b>103.0</b>	<b>99.0</b>
Compaction Method	<b>Standard</b>	<b>Standard</b>	<b>Standard</b>
Report Remarks	**	**	**

## Moisture Variation Note:

Positive values = test is dry of OMC  
 Negative values = test is wet of OMC



# Material Test Report



**Report Number:** GS6110/1-3  
**Issue Number:** 1  
**Date Issued:** 21/01/2022  
**Client:** BildGroup  
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061  
**Contact:** Sharon  
**Project Number:** GS6110/1  
**Project Name:** Lucas Grange Estate - Stage 2F (Level 1)  
**Project Location:** Ballarat  
**Work Request:** 6536  
**Date Sampled:** 18/01/2022 7:30  
**Dates Tested:** 18/01/2022 - 20/01/2022  
**Sampling Method:** AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted  
**Specification:** 95% Standard Compaction & +/- 3% Moisture Variation  
**Location:** Lucas Grange  
**Material:** Silty CLAY, medium to high plasticity, brown  
**Material Source:** On-site

Ground Science Pty Ltd  
 Ground Science Laboratory  
 13 Brock Street Thomastown Victoria 3074  
 Phone: (03) 9464 4617  
 Email: brent@groundscience.com.au

Accredited for compliance with ISO/IEC 17025 - Testing



*Brent Elliott*

Approved Signatory: Brent Elliott  
Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1				
Sample Number	61101-S7	61101-S8	61101-S9	61101-S10
Date Tested	18/01/2022	18/01/2022	18/01/2022	18/01/2022
Time Tested	08:52	09:15	09:26	09:31
Test Request #/Location	Retest of 5	From s/w corner of lot 224	From s/w corner of lot 223	From s/w corner of lot 223
Latitude	**	15m east	7m east	15m east
Longitude	**	3m north	3m north	3m north
Layer / Reduced Level	1	2	3	4
Thickness of Layer (mm)	200	150	150	150
Soil Description	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown
Test Depth (mm)	175	125	125	125
Sieve used to determine oversize (mm)	19.0	19.0	19.0	19.0
Percentage of Wet Oversize (%)	0	5	0	0
Field Wet Density (FWD) t/m <sup>3</sup>	1.93	1.93	1.89	1.88
Field Moisture Content %	23.2	24.2	22.6	26.5
Field Dry Density (FDD) t/m <sup>3</sup>	1.57	1.56	1.54	1.49
Peak Converted Wet Density t/m <sup>3</sup>	1.99	**	1.88	1.90
Adjusted Peak Converted Wet Density t/m <sup>3</sup>	**	1.90	**	**
Moisture Variation (Wv) %	0.0	**	2.5	0.5
Adjusted Moisture Variation %	**	2.5	**	**
Hilf Density Ratio (%)	<b>97.0</b>	<b>101.5</b>	<b>100.5</b>	<b>99.0</b>
Compaction Method	<b>Standard</b>	<b>Standard</b>	<b>Standard</b>	<b>Standard</b>
Report Remarks	**	**	**	**

**Moisture Variation Note:**

Positive values = test is dry of OMC  
 Negative values = test is wet of OMC

# Material Test Report



**Report Number:** GS6110/1-4  
**Issue Number:** 1  
**Date Issued:** 20/05/2022  
**Client:** BildGroup  
 7 Metrolink Circuit, Campbellfield, Melbourne VIC 3061  
**Contact:** Ben  
**Project Number:** GS6110/1  
**Project Name:** Lucas Grange Estate - Stage 2F (Level 1)  
**Project Location:** Ballarat  
**Work Request:** 8452  
**Date Sampled:** 18/05/2022 13:00  
**Dates Tested:** 18/05/2022 - 19/05/2022  
**Sampling Method:** AS 1289.1.2.1 6.4 (b) - Sampling from layers in earthworks or pavement - compacted  
**Specification:** 95% Standard Compaction & +/- 3% Moisture Variation  
**Location:** Ballarat  
**Material:** Silty CLAY, medium to high plasticity, brown

Ground Science Pty Ltd  
 Ground Science Laboratory  
 13 Brock Street Thomastown Victoria 3074  
 Phone: (03) 9464 4617  
 Email: brent@groundscience.com.au



Accredited for compliance with ISO/IEC 17025 - Testing

Approved Signatory: Brent Elliott  
 Laboratory 21C

NATA Accredited Laboratory Number: 15055

Compaction Control AS 1289 5.7.1 & 5.8.1 & 2.1.1					
Sample Number	61101-S11	61101-S12	61101-S13	61101-S14	61101-S15
Date Tested	18/05/2022	18/05/2022	18/05/2022	18/05/2022	18/05/2022
Time Tested	13:41	13:55	14:07	14:15	14:25
Test Request #/Location	From n/w corner of lot 236	From n/w corner of lot 235	From n/w corner of lot 234	From n/w corner of lot 213	From n/w corner of lot 214
Latitude	5m south	3m south	5m south	3m south	5m south
Longitude	3m east	3m east	3m east	25m east	25m east
Layer / Reduced Level	1	2	3	2	1
Thickness of Layer (mm)	150	150	150	150	150
Soil Description	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown	Silty CLAY, medium to high plasticity, brown
Test Depth (mm)	125	125	125	125	125
Sieve used to determine oversize (mm)	19.0	19.0	19.0	19.0	19.0
Percentage of Wet Oversize (%)	4	3	1	0	0
Field Wet Density (FWD) t/m <sup>3</sup>	2.14	2.05	2.11	1.84	1.87
Field Moisture Content %	19.7	24.2	20.7	28.7	28.0
Field Dry Density (FDD) t/m <sup>3</sup>	1.79	1.65	1.75	1.43	1.46
Peak Converted Wet Density t/m <sup>3</sup>	**	**	**	1.82	1.82
Adjusted Peak Converted Wet Density t/m <sup>3</sup>	2.08	2.00	2.13	**	**
Moisture Variation (Wv) %	**	**	**	3.0	3.0
Adjusted Moisture Variation %	0.5	0.5	-0.5	**	**
Hilf Density Ratio (%)	<b>103.5</b>	<b>102.5</b>	<b>99.5</b>	<b>101.0</b>	<b>102.5</b>
Compaction Method	<b>Standard</b>	<b>Standard</b>	<b>Standard</b>	<b>Standard</b>	<b>Standard</b>
Report Remarks	**	**	**	**	**

**Moisture Variation Note:**

Positive values = test is dry of OMC  
 Negative values = test is wet of OMC

## **APPENDIX C**

Site Photographs

21 Dec 2021 at 11:35:35 am  
152° SE  
Lucas VIC 3350  
Australia  
Proofroll over stage 2F

